



# Implementation Status Update

5/13/2019



# P2G Implementation Timeline



## March 5-8

- ✓ Implementation Kick-off
- ✓ Principal placements
- ✓ Special Ed self-contained placements

## March 11-15

- ✓ CTE courses determined


## March 18-22

- ✓ Spring Break




## April 1-5

- ✓ Affected Special Ed, CC teachers, counselors, LMS placed

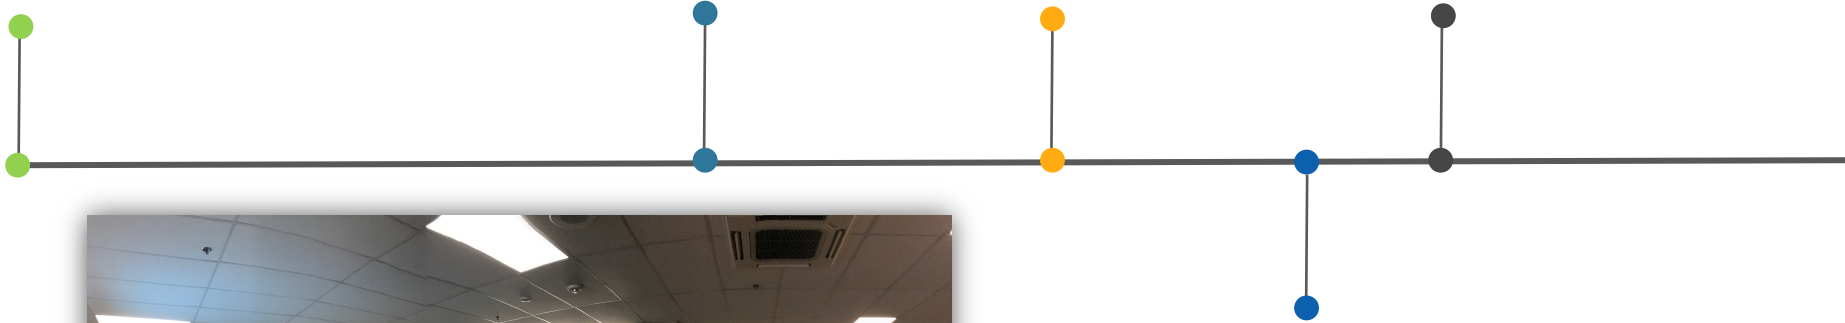

## March 25-29

- ✓ Assistant Principal placements
- ✓ Family notification letters sent

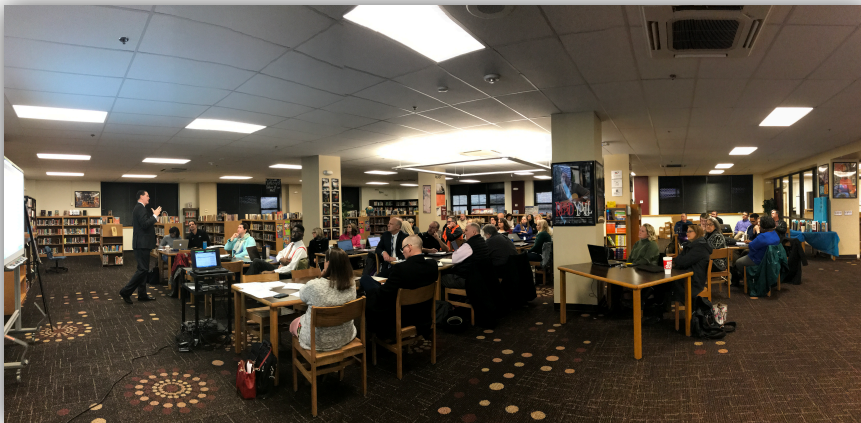



# P2G Implementation Timeline



## April 15-19

- ✓ Application school deadline
- ✓ NCC & normal hiring resumes
- ✓ Round 1 - affected support staff placed

## April 29-May 3

- ✓ HS students rolled over in Infinite Campus
- ✓ Administrative staff moves begin

## May 13-17

- ☐ Outdated records disposal

## April 8-12

- ✓ 2019-20 room assignments
- ✓ Publish moving guide to staff
- ✓ Student Transfer application deadline



May 4 - Districtwide Open House

## May 6-10

- ✓ Begin building modifications
- ✓ Academic/Library moves begin
- ✓ Media, Title I support staff placed



# P2G Implementation Timeline



## May 20-24

- Transfers notified, IC roll-over
- Nurse staffing completed
- Bus routes completed
- PTA, partner transitions

## June 3-7

- Secondary master schedules completed
- Classroom moves begin
- Board meeting moves to MetroTech SL

## July 1-12

- Moves in progress
- Building mods in progress


## May 27-31

- More building modifications begin
- POs closed for closing sites

## June 10-28

- Moves in progress
- Building mods in progress
- 25<sup>th</sup> - Allocate remaining funds to follow students
- 28<sup>th</sup> - District equipment removed from facilities to be repurposed for Day One

May 24 – Last Day for Students

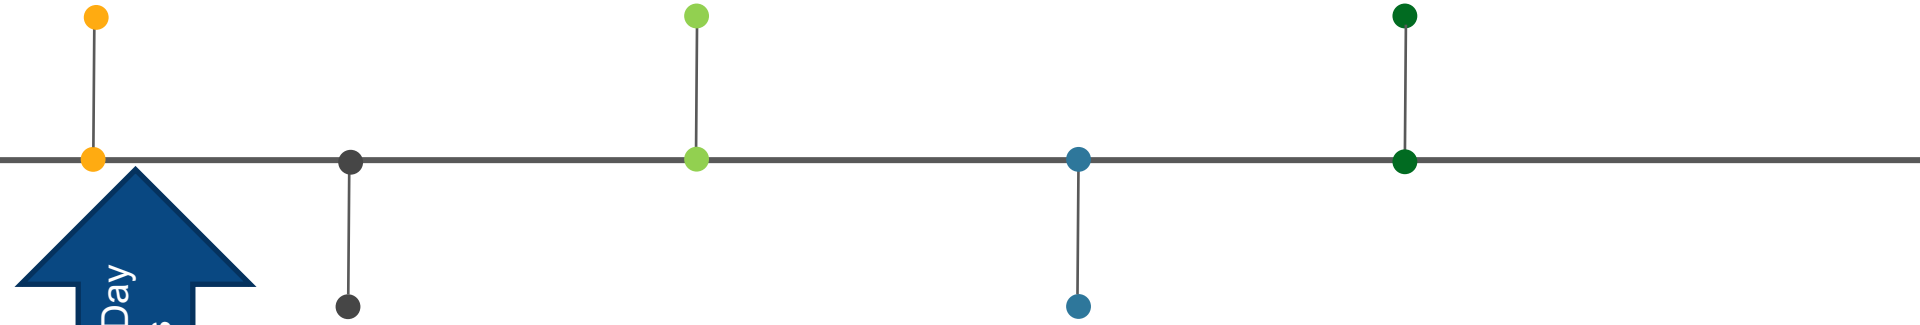



# P2G Implementation Timeline



July 30 –  
Teachers return

July 31-August 2

- ❑ Verification and adjustments



August 12  
Students return

August 12 →

- ❑ Ongoing/Phase 2 projects
- ❑ Monitoring
- ❑ Lessons learned
- ❑ Adjustments as needed

July 15-30

- ❑ Walk-through school readiness checklists completed
- ❑ 26<sup>th</sup> – secondary student schedules completed

August 5-9


- ❑ Team-building & professional learning
- ❑ School-based events
- ❑ Completion of any outstanding school-readiness projects






# 2019-20 Staffing (as of 5/9/2019)


### Principals




### Teachers\*



\* "Teachers" includes other certified staff (e.g. counselors, librarians)



### Assistant Principals




### Nurses




# Facilities (as of 5/9/2019)

## Trade-Up Rooms Identified

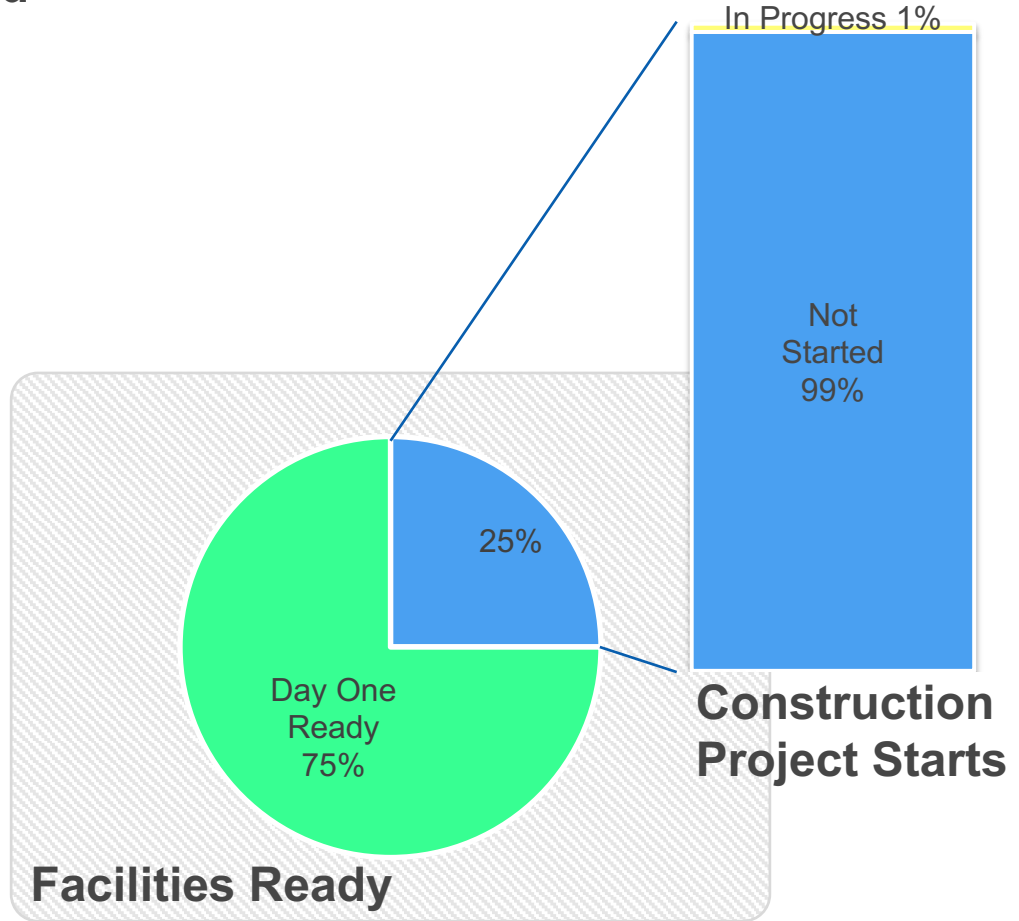



# Repurposing (as of 5/9/2019)

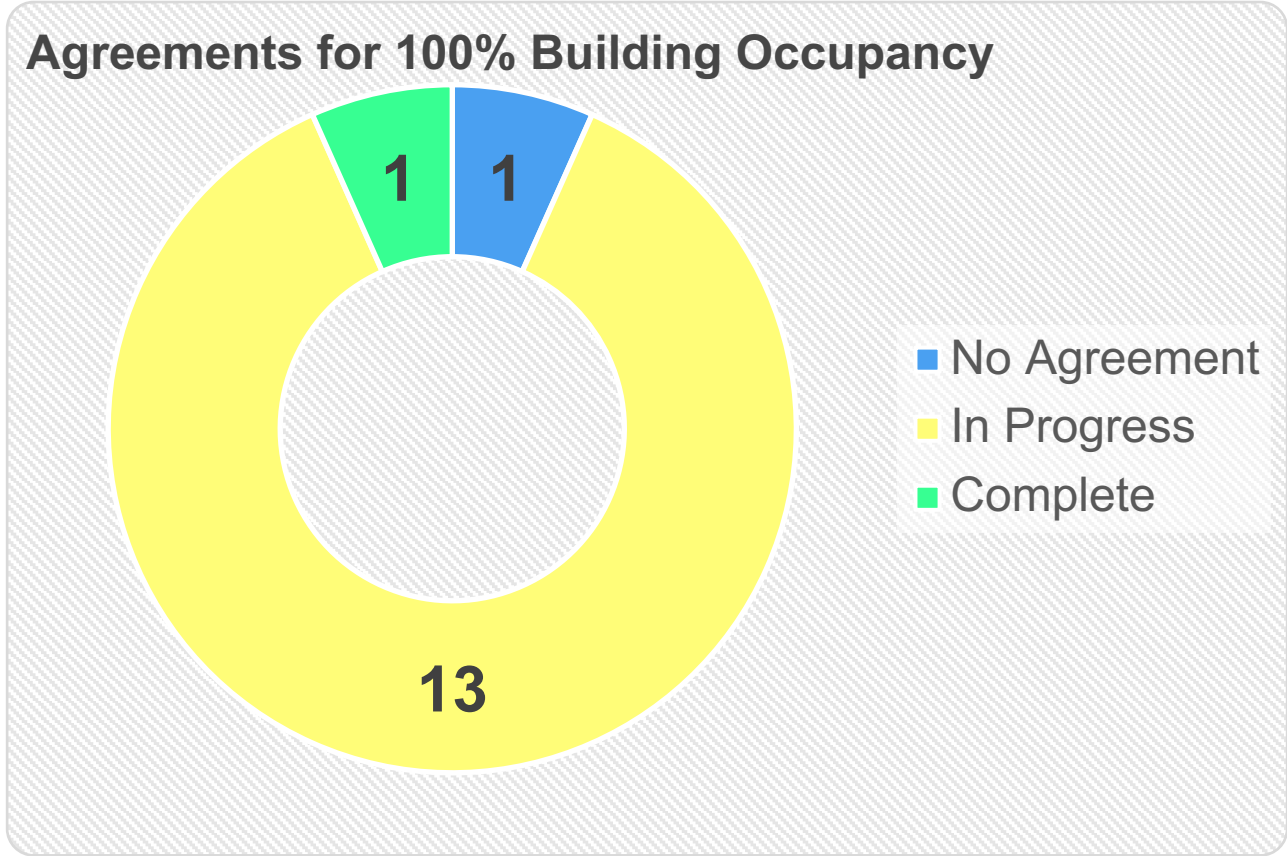



[www.okcps.org/PathwayProject](http://www.okcps.org/PathwayProject)

**PATHWAY**

TO

**GREATNESS**
